

工程部週報

2026/09/07 ~ 2026/09/11



兆豐銀行 - 宏明

■ 工程事項：

1. 支架組裝 26% (鋼構鏽點除鏽、清潔、上高鋅漆兩層 完成 50%)
2. 模組安裝 26% (模組板上棚架 130 / 414、模組螺絲定磅 0%、吊掛進料完成)
3. 變流器安裝 90% (安裝固定完成尚未結線測試)
4. 儲能櫃安裝 10%
(吊掛進料完成、監控拉線測試 0%、電纜接線 0%、充放電測試 0%)


■ 追蹤事項：

1. 追蹤後續監控螢幕、AC 盤體 ... 等物料進場及施工人員進場

模組安裝



螢幕、ACP箱體

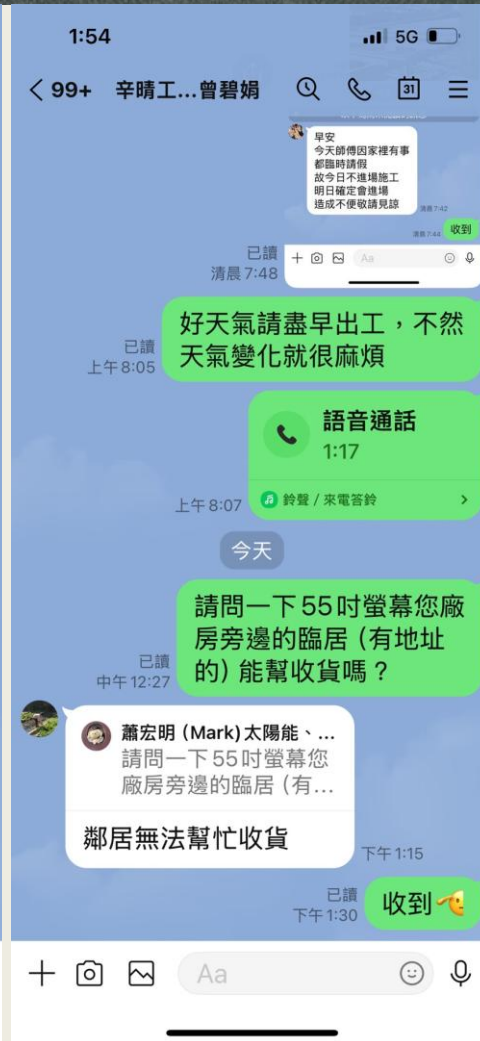

台以八翁 - 宏明

- 工程事項：

1. 9/2 辦公室漏水，貼鋁箔膠帶

- 追蹤事項：

1. 漏水 8/25 提報、施工工法及工序建議，內部審核中 (第 16 天)

法蘭摩沙 - 鎮寶、名淙、俊雄

F 區配管進度 100%

拉線進度 91%

絕緣導通測試 70%


儀表安裝 91%

儀表結線 62%

總進度 87.1%

施工進度表

五 JB箱至PLC拉設								
1	配管	20	2025/12/12	2025/12/31	100%	20	2025/12/12	2025/12/31 100%
2	配線槽	45	2025/12/29	2026/2/11	100%	45	2025/12/29	2026/2/11 100%
3	拉線	190	2026/1/7	2026/7/15	100%	210	2026/1/20	2026/8/17 100%
4	絕緣/導通測試	150	2026/2/26	2026/7/25	100%	193	2026/3/3	2026/9/11 90%
5	盤體結線	140	2026/3/10	2026/7/27	100%	173	2026/3/23	2026/9/11 90%
六 F區(110區)								
1	JB安裝	30	2025/12/1	2025/12/30	100%	30	2025/12/1	2025/12/30 100%
2	RSG配管	120	2026/4/5	2026/8/2	100%	131	2026/4/12	2026/8/20 100%
3	拉線	150	2026/4/16	2026/9/12	98%	150	2026/4/23	2026/9/19 91%
4	絕緣/導通測試	20	2026/8/17	2026/9/5	100%	73	2026/7/1	2026/9/11 70%
5	儀表安裝	130	2026/5/20	2026/9/26	87%	116	2026/5/28	2026/9/20 91%
6	安裝Tube	80	2026/7/10	2026/9/27	30%	83	2026/7/10	2026/9/30 30%
7	儀表結線	30	2026/9/1	2026/9/30	28%	92	2026/7/1	2026/9/30 62%
七 測試驗收								
1	迴路測試	15	2026/9/30	2026/10/14	0%	15	2026/9/30	2026/10/14 0%
2	功能測試	15	2026/9/30	2026/10/14	0%	15	2026/9/30	2026/10/14 0%
3	驗收及結案報告	30	2026/10/1	2026/10/30	0%	30	2026/10/1	2026/10/30 0%
		343		87.6%		343		87.1%



										點位	二次側					盤數	一次側				
											配管	配線	導通&絕緣	箱體結線	儀表結線		配管	配線	導通&絕緣	結線	
6F	SAJB 11006	AJB 11002	DJB 11019	DJB 11010							37	37	37	37	37		4	4	4	4	
		24	10	3					數量：	37						4					
5F	SAJB 11005	DJB 11017	DJB 11009	AJB 11019	AJB 11021	AJB 11020	DJB 11018				115	115	115	115			7	7	7	7	
		14	15	24	23	24	15		數量：	115						7					
4F	SIDJB 11006	DJB 11015	APJB 11004	AJB 11017	DJB 11008	DJB 11014					199	199	199	199		12	12	12	12		
	8	20	9	24	18	17															
	DJB 11013	AJB 11016	DJB 11007	AJB 11018	DJB 11016																
	20	24	15	24	20			數量：	199						12						
3F	SIDJB 11005	AJB 11012	APJB 11003	DFJB 11004	DJB 11009	DJB 11006					319	319	319	41		18	18	18	18		
	17	23	14	12	18	12															
	DJB 11010	AJB 11010	DJB 11004	DJB 11008	DJB 11012	AJB 11014															
	17	24	11	19	15	24															
	DJB 11005	AJB 11011	AJB 11013	DJB 11011	AJB-11015																
	17	24	24	24	24			數量：	319						18						
2F	SAJB 11002	SIDJB 11003	SIDJB 11004	DFJB 11003	APJB 11002	DJB 11003	AJB 11009				279	210	76	118	24		14	14	14	14	
		16	22	16	15	21	24														
	DJB-11004	DJB 11005	DJB-11006	DJB 11007	AJB-11006	AJB 11007	AJB 11008														
	24	23	23	23	24	24	24		數量：	279											14
1F	SAJB 11001	SIDJB 11001	SIDJB 11002	DJB-11001	DJB 11002	AJB-11023					351	47		48		18	18		18		
		7	19	10	17	17	14														
	DFJB 11001	APJB 11001	DFJB 11002	DJB 11001	DJB 11002	DJB 11003	DJB-11020														
	24	17	19	24	23	24	19														
	AJB 11001	AJB 11002	AJB 11003	AJB 11004	AJB11005				數量：	351										18	
	22	24	24		23	24															
									總數	1300	1300	927	746	558	61	73	73	73	55	73	
F區儀表		總數		到料		已完成		拉線		配管		儀錶安裝		導通&絕緣		結線					
		565		565		512		0.91		1.00		0.91		0.70		0.62					

儀表安裝、配管工程



儀表安裝、配管工程

