

工程部週報

2026/09/21 ~ 2026/09/24



施工報告

F區配管進度 :100%

拉線進度 :99%

絕緣導通測試:100%

儀表安裝 :97%

儀表結線 :72%

總進度 :88.9%

案場協調項目 :

1. 7月提供亞通管路組儀表無法安裝餘13處


2. 9/17日亞通管路組提TIT(溫度傳訊器)餘30處

公司部門協調項目:無

窒礙難行項目 :無





施工進度表

2025/12/12	2025/12/31	100%	20	2025/12/12	2025/12/31	100%
2025/12/29	2026/2/11	100%	45	2025/12/29	2026/2/11	100%
2026/1/7	2026/7/15	100%	210	2026/1/20	2026/8/17	100%
2026/2/26	2026/7/25	100%	200	2026/3/3	2026/9/18	100%
2026/3/10	2026/7/27	100%	195	2026/3/23	2026/10/3	90%
2025/12/1	2025/12/30	100%	30	2025/12/1	2025/12/30	100%
2026/4/5	2026/8/2	100%	131	2026/4/12	2026/8/20	100%
2026/4/16	2026/9/12	100%	160	2026/4/23	2026/9/29	99%
2026/8/17	2026/9/5	100%	87	2026/7/1	2026/9/25	100%
2026/5/20	2026/9/26	98%	130	2026/5/28	2026/10/4	97%
2026/7/10	2026/9/27	30%	100	2026/7/10	2026/10/17	30%
2026/9/1	2026/9/30	79%	110	2026/7/1	2026/10/18	72%
2026/9/30	2026/10/14	0%	15	2026/10/18	2026/11/1	0%
2026/9/30	2026/10/14	0%	15	2026/10/18	2026/11/1	0%
2026/10/1	2026/10/30	0%	30	2026/10/1	2026/10/30	0%
343			89.4%	343		
				88.9%		



										二次側					盤
									點位	配管	配線	導通&絕緣	箱體結線	儀表結線	
6F	SAJB 11006	AJB 11022	D/B 11019	UB 11010					數量: 37	37	37	37	37	37	
5F	SAJB 11005	D/B 11017	UB 11009	AJB 11019	AJB 11021	AJB 11020	D/B 11018		數量: 115	115	115	115	115		
4F	SID/B 11006	D/B 11015	APJB 11004	AJB 11017	UB 11008	D/B 11014				199	199	199	199		
	8	20	9	24	18	17									
	D/B 11013	AJB 11016	UB 11007	AJB 11018	D/B 11016				數量: 199						
3F	SID/B 11005	AJB 11012	APJB 11003	DPJB 11004	D/B 11009	UB 11006				319	319	319	319	69	
	17	23	14	12	18	12									
	D/B 11010	AJB 11010	UB 11004	D/B 11008	D/B 11012	AJB 11014									
	17	24	11	19	15	24									
	UB 11005	AJB 11011	AJB 11013	D/B 11011	AJB-11015										
2F	SAJB 11002	SID/B 11003	SID/B 11004	DPJB 11003	APJB 11002	UB 11003	AJB 11009			279	264	279	279	48	
		16	22	16	15	21	24								
	D/B-11004	D/B 11005	D/B-11006	D/B 11007	AJB-11006	AJB 11007	AJB 11008								
	24	23	23	23	24	24	24	數量: 279							
1F	SAJB 11001	SID/B 11001	SID/B 11002	UB-11001	UB 11002	AJB-11023				351	310	351	48	14	
	7	19	10	17	17	14									
	DPJB 11001	APJB 11001	DPJB 11002	D/B 11001	D/B 11002	D/B 11003	D/B-11020								
	24	17	19	24	23	24	19								
	AJB 11001	AJB 11002	AJB 11003	AJB 11004	AJB-11005			數量: 351							
總數										1300	1300	1244	1300	997	168
F區儀表		總數	到料	已完成	拉線		配管		儀錶安裝	導通&絕緣					
		571	571	556	0.99		1.00		0.97	1.00					

儀表安裝、配管工程

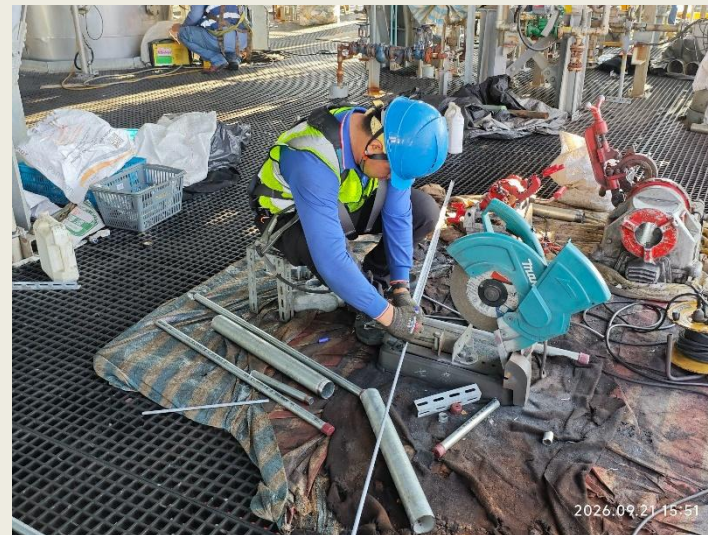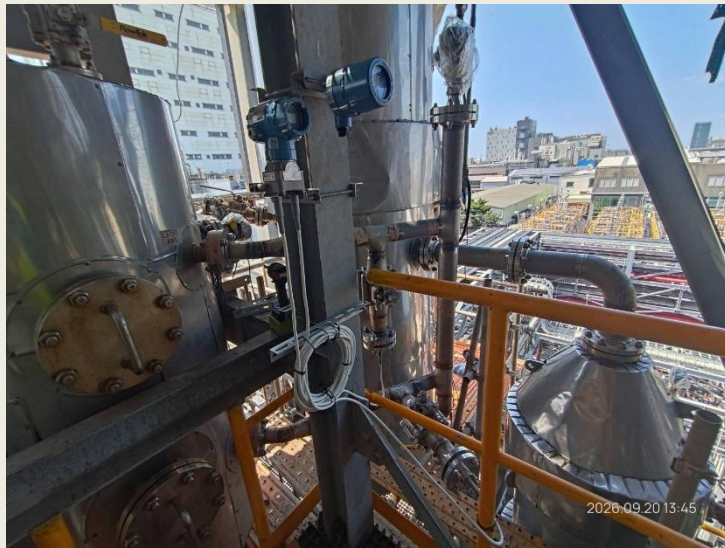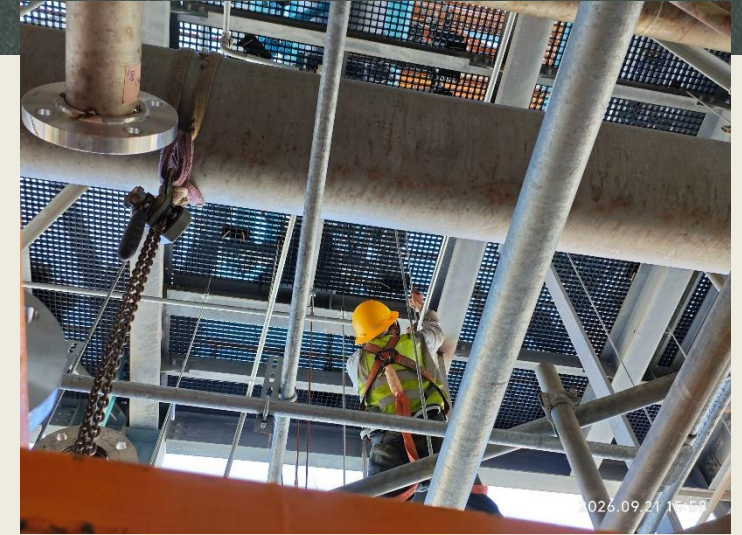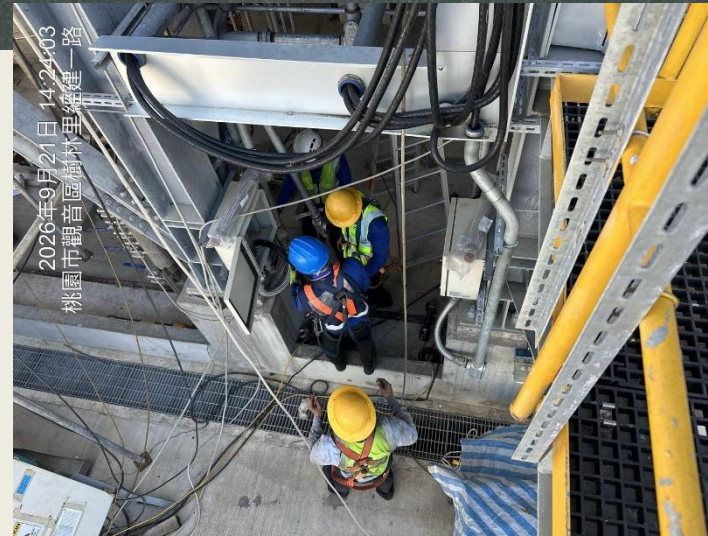

儀表安裝、配管工程

